RI/FS Project Schedule
Leviathan Mine Site
Alpine County, California

ID	Task Name
1	**RI/FS Work Plans**
2	Supplement to PWP
3	Background/Reference FRI WP
4	On-Property FRI WP
5	Off-Property FRI WP
6	Supplement to On-Property FRI WP
9	Supplement for Off-Property FRI WP
12	HHRA WP
13	ERA WP
14	**Mapping and Well FRIs**
15	Topographic Mapping
16	Geologic Mapping
17	Mapping Downstream
18	Hyderspectral/Lidar
19	Well Reconnaissance
20	Well Rehabilitation/Completion
21	Groundwater Monitoring
30	**Background FRI**
31	Surface Water Sampling and Analysis
34	Sediment Sampling and Analysis 1
35	Sediment Sampling and Analysis 2
36	Groundwater Sampling and Analysis
44	Soil Sampling and Analysis
45	Plant Sampling and Analysis
48	Fish Sampling and Analysis
49	**On-Property FRI**
50	Water Balance
53	Bioassessement
54	Surface Water and Sediment
57	Hydrogeology
58	Geotechnical
62	Stormwater
67	Source Investigation
68	**Off-Property FRI**
69	Habitat Verification
70	Plant Sampling
71	Soil Sampling 1
72	Soil Sampling 2
73	Plant Sampling 1
74	Plant Sampling 2
75	Bioassay Sampling
78	Soil Sampling
81	Sediment Sampling
84	Surface Water Sampling
85	Surface Water Sampling 1
86	Surface Water Sampling 2
87	Surface Water Sampling 3
88	**RI/FS Reporting**
89	Quarterly Progress Reports
109	Technical Memorandum-Well FRI
110	Mapping FRI
111	Background FRI
112	Groundwater Monitoring Reports
121	RI/FS Data Summary Reports
125	RI Draft Report
126	Draft HHRA
127	Draft ERA
128	**Feasibility Study**
129	Treatability Studies
130	Detailed Identification Contamination/Hazards
131	Identification of Remedial Action Alternatives
132	Evaluation of Alternatives
133	Feasibility Study Report

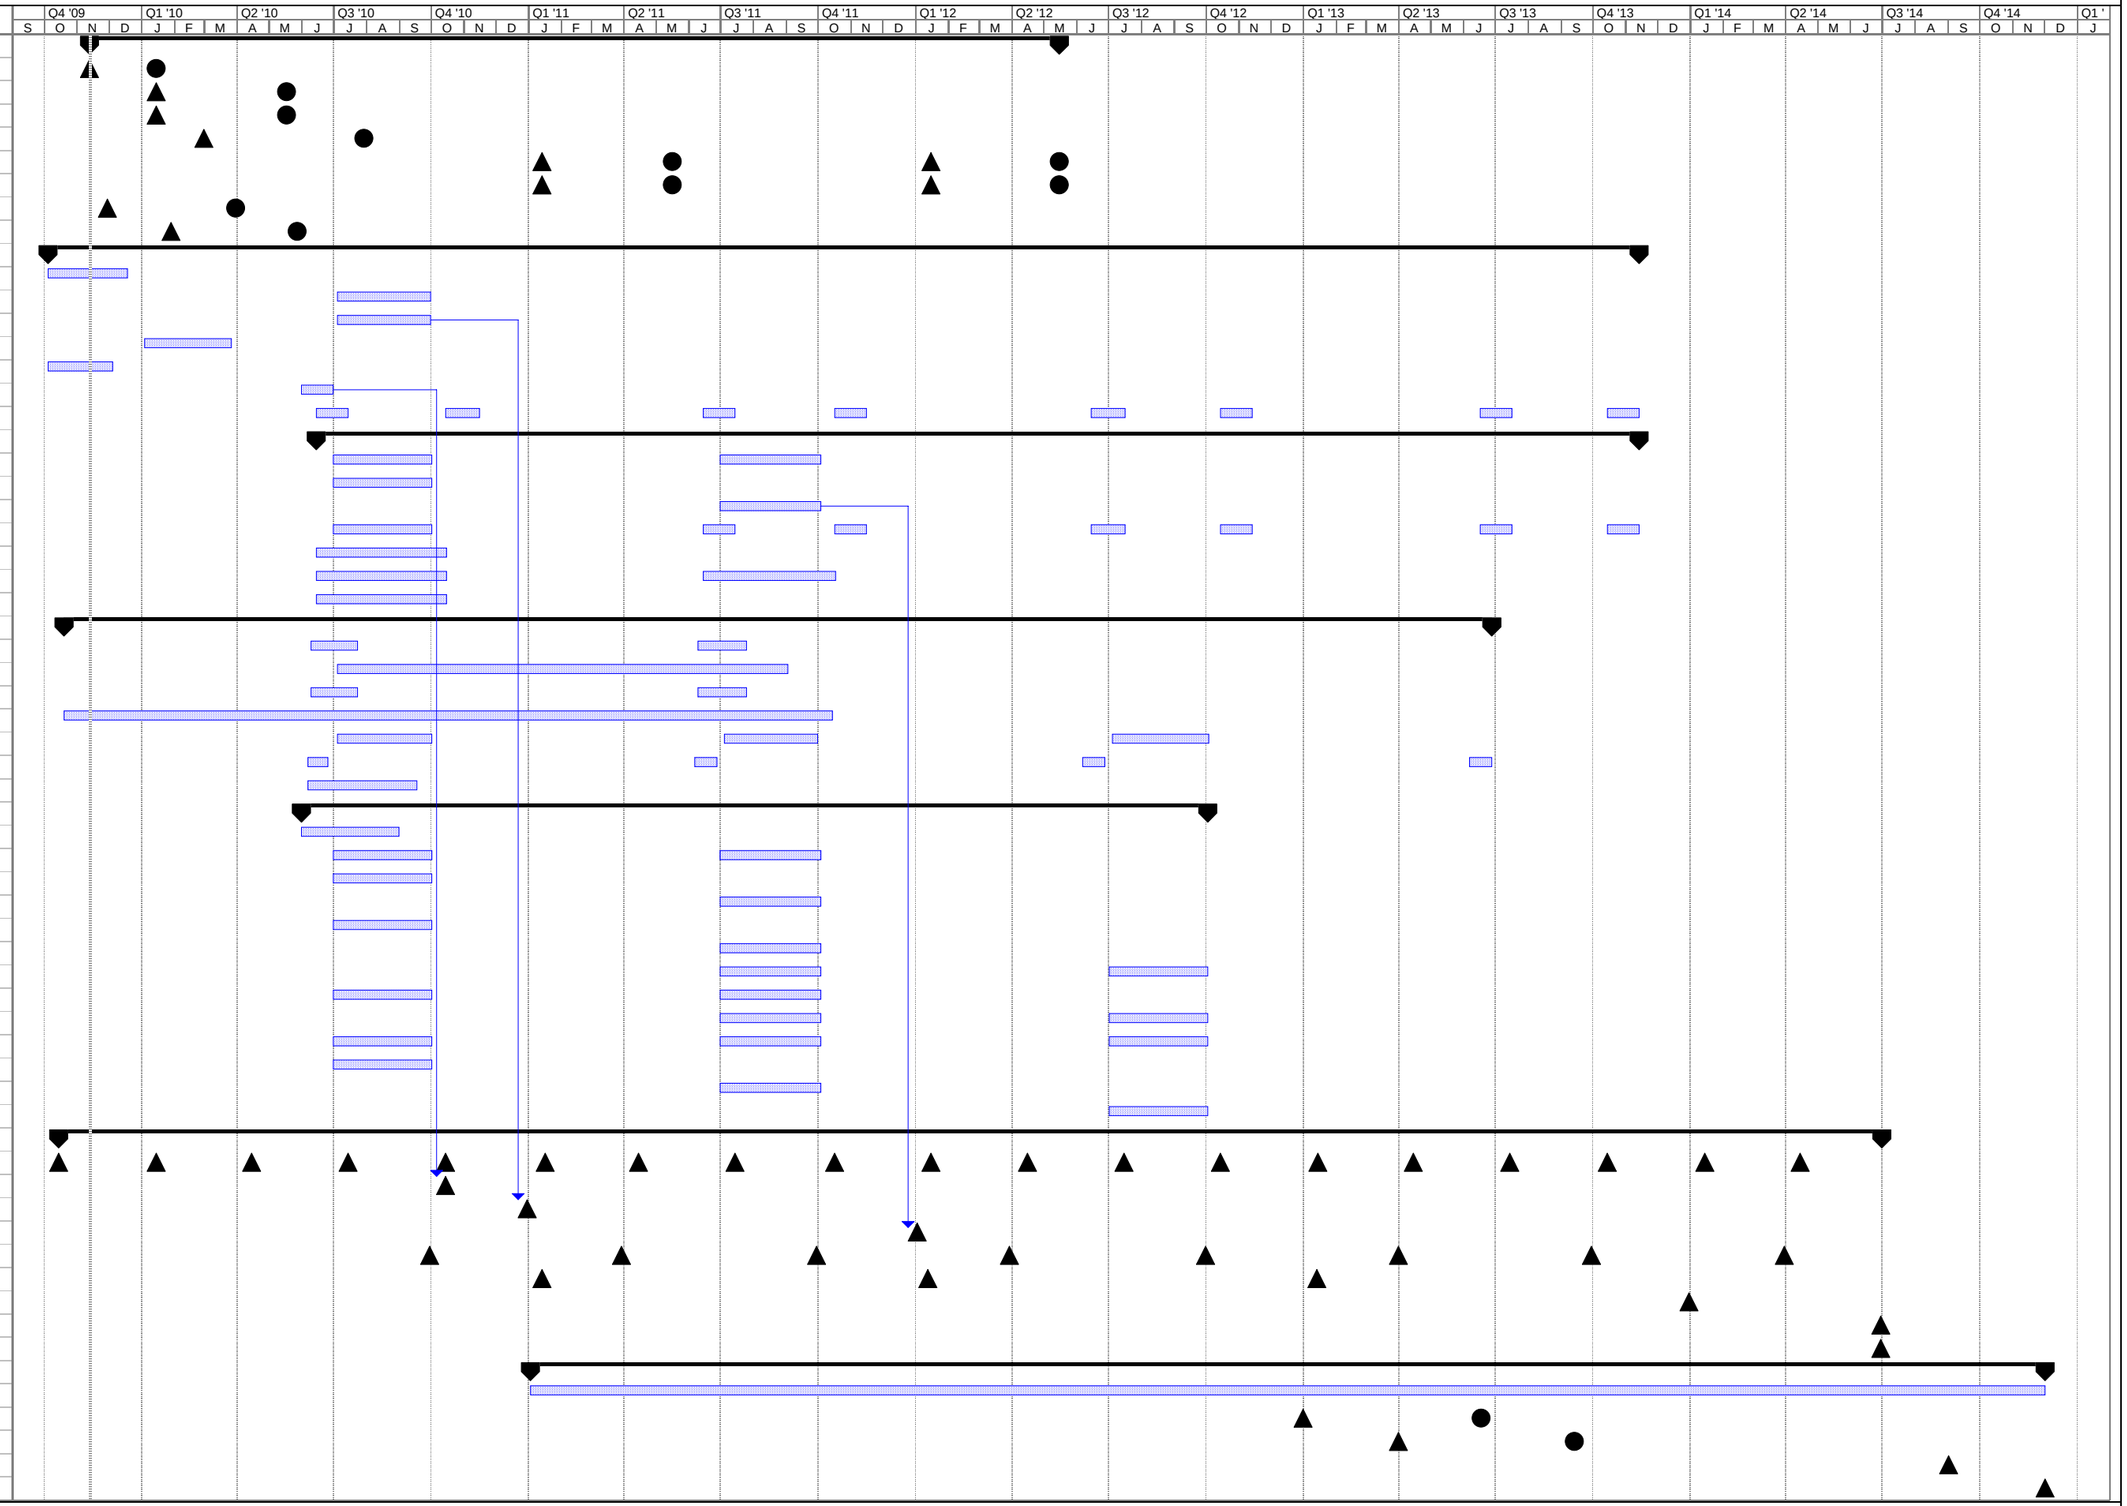

Project: Leviathan Mine RI/FS
Date: Fri 11/13/09

Task | Summary | Submittal | Expected EPA Approval

task_schedule_111309.mpp
